IT505 Group Project

NorthStar Digital
Personal Health Companion App

Project Management Report

Prepared by:

Pooja Sharma
Oji Nkechi
Oluwakayode Soyinka
Dominick Tressler

Concordia University of Edmonton
March 31, 2026

Table of Contents

Chapter 1 - Project Charter
Chapter 2 - Scope Planning
Chapter 3 - Schedule Planning
Chapter 4 - Risk Identification & Analysis
Chapter 5 - Stakeholder Analysis
References22

Chapter 1 - Project Charter

Project Title	NorthStar Digital - Personal Health Companion App (MVP)
Project Start Date	April 1, 2026
Projected Finish Date	July 31, 2026
Project Manager	Oji Nkechi
Date	March 26, 2026

1.1 Budget Information

The total estimated budget for this project is $200,000, allocated as follows:

- Project Management - $25,000
- Mobile Development - $90,000
- UI/UX Design - $25,000
- Quality Assurance - $25,000
- Marketing & Launch - $20,000
- Contingency Reserve - $15,000

1.2 Project Objectives

- Develop a mobile health companion application within a 4-month timeline.
- Provide users with tools to track basic health metrics (blood pressure, weight, exercise).
- Enable medication reminders with notification and scheduling.
- Allow users to store medical contacts and emergency health information.
- Launch a Minimum Viable Product (MVP) to gather early user feedback.
- Ensure the app is simple, accessible, and user-friendly, especially for older adults.

1.3 Success Criteria

- Project is completed within 4 months (within schedule).
- Total cost does not exceed $200,000 (within budget).
- All core features function correctly on both Android and iOS platforms.
- App meets usability and accessibility requirements.
- No critical security or privacy issues are present.
- MVP is successfully launched and user feedback is collected.

1.4 Project Approach

The project will follow an Agile development approach, allowing iterative development and continuous feedback throughout the project lifecycle. Major phases will include:

1. Project initiation and planning
2. Requirements gathering and scope definition
3. UI/UX design and prototyping
4. Incremental development of core features
5. Testing and quality assurance
6. MVP launch and feedback collection

A small cross-functional team will collaborate closely, with regular progress reviews and sprint cycles to ensure timely delivery.

1.5 Roles and Responsibilities

Name	Role	Position	Contact
Oji Nkechi	Project Manager	Project Lead	See project directory
-	Mobile Developer	Development Team	-
-	UI/UX Designer	Design Team	-
-	QA Lead	Testing Team	-
-	Marketing Representative	Marketing Team	-

1.6 Comments

This project represents a strategic opportunity for NorthStar Digital to enter the digital health market with a focused and user-friendly solution. By maintaining a clear scope and emphasizing usability and privacy, the team aims to deliver a high-quality product that meets user needs and supports future expansion.

Chapter 2 - Scope Planning

2.1 Introduction

The purpose of this project is to develop a mobile application that enables users, in particular older adults, to manage their basic health metrics, track medication schedules, and store vital medical information. The project aims to deliver a Minimum Viable Product (MVP) within a four-month timeframe to help test market demand and to gather early feedback.

2.2 Project Scope Statement

Project Objectives

Develop a reliable, simple mobile health management app for Android and iOS within four months.

In-Scope Features

- Health Tracker: Recording blood pressure, exercise, weight, and general well-being notes.
- Medication Reminder: scheduling, notifications, and medication notes.
- Medical Contacts Directory: storage for doctors, clinics, pharmacies, and emergency contacts.
- Emergency Information Card: quick access to allergies, blood type, and medical conditions.

Out-of-Scope

The following are explicitly excluded from the initial release:

- Advanced diagnostic tools
- Wearable hardware integration (e.g., smartwatches)
- Desktop and web-based versions

Design Requirements

The app must feature large readable fonts, clear navigation, and a secure, privacy-conscious architecture.

2.3 Work Breakdown Structure (WBS)

The Work Breakdown Structure (WBS) breaks the project down into manageable components and tasks, organized by functional area.

WBS ID	Component	Tasks / Deliverables
1	**Project Management**	
1.1	Initiation	Project charter; stakeholder analysis
1.2	Sprint Planning	Agile sprint planning; backlog management
2	**UI/UX Design**	
2.1	Interface Design	User interface design with focus on accessibility and large fonts
2.2	Prototype	Navigation flow and prototype development
3	**App Development**	
3.1	Health Tracker	Health tracker module development
3.2	Medication Reminder	Medication reminder logic and notifications
3.3	Contacts & Emergency Card	Medical contacts and emergency card database
4	**Quality Assurance**	
4.1	Cross-Platform Testing	Testing on Android and iOS devices
4.2	Accessibility Testing	Accessibility and usability testing
5	**Deployment & Launch**	
5.1	App Store Submission	App Store and Google Play submission
5.2	Feedback Collection	Early adopter feedback collection

2.4 Verifying Completion of Project Deliverables

Deliverables will be formally reviewed and accepted to ensure they meet project requirements. The verification process includes:

- Conducting regular reviews at the end of each phase or sprint.
- Comparing completed deliverables against acceptance criteria.
- Performing testing (functional, usability, and compatibility testing).
- Obtaining approval from stakeholders (e.g., project sponsor or client).
- Documenting acceptance or required revisions.

Only deliverables that meet agreed-upon standards will be considered complete.

2.5 Managing Requests for Changes to Project Scope

As an Agile project, changes will be managed through the following process:

- Change Request: Any new feature request (beyond the core tracker and reminders) will be documented in the product backlog.
- Impact Assessment: The Project Manager will evaluate the impact on the $200,000 budget and the 4-month timeline.
- Prioritization: If a change is approved, a lower-priority MVP feature may be moved to a later version to keep the release date intact.

Chapter 3 - Schedule Planning

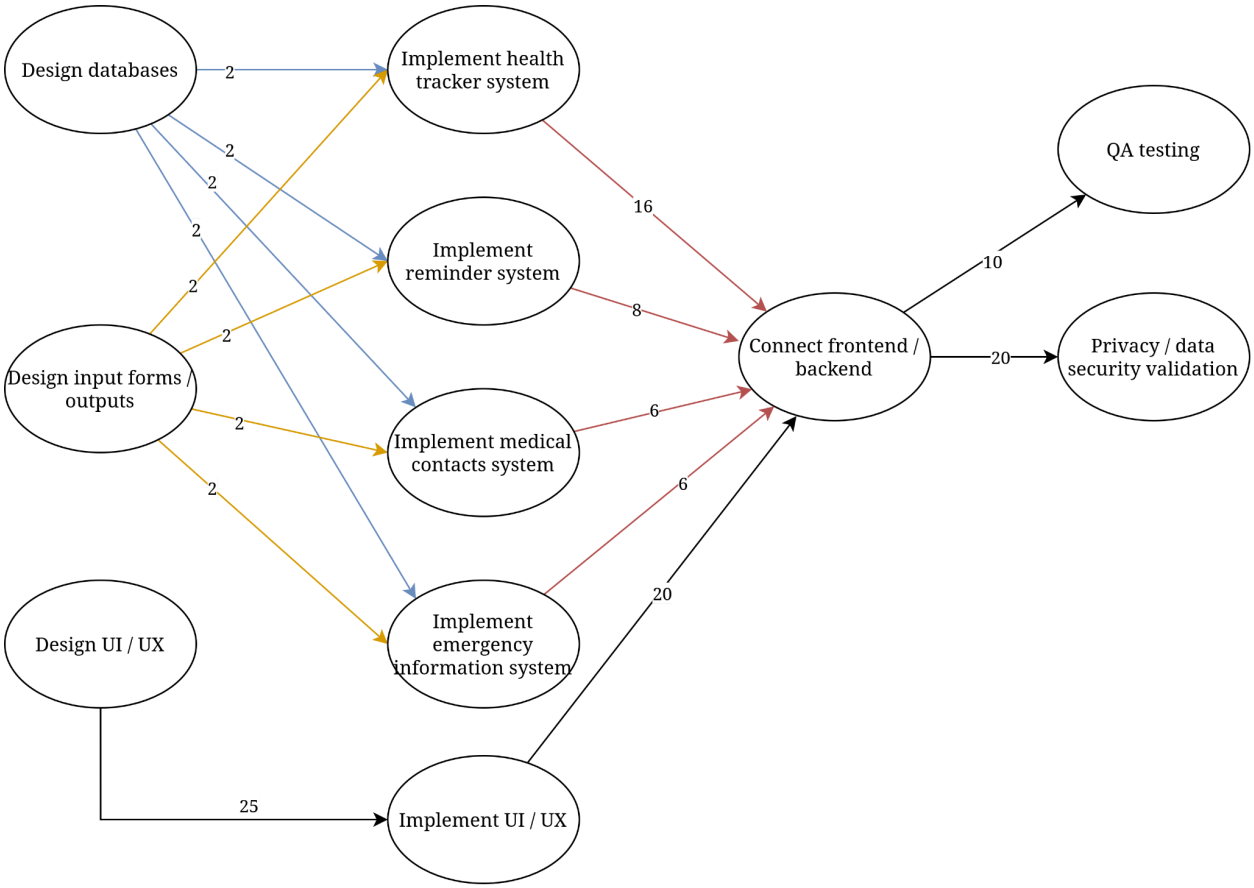

			Total hours->	165	68	45	50	**328**
Major tasks	**Start Date**	**End Date**	**Responsible**	**Estimated Hours per person**				**Total**
				Project Manager (PM)	**Mobile Dev (MD)**	**UI / UX**	**QA**	**Est. Hours**
1.1 Initiating	Week 1	Week 2						
1.1.1 Project charter (PR1)			PM	20				
1.1.2 Kick-off meeting (PR1)			PM	6				
1.1.3 Team MBTI summary (PR1)			PM	3				
1.1.4 Sponsor feedback (PR1)			PM	3				
1.1.5 Google site initial set-up (PR1)			PM	8				
1.2 Planning	Week 2	Week 3						
1.2.1 Draft scope statement (PR1)			PM	5				
1.2.2 Team contract (PR1)			PM	16				
1.2.3 Excel draft schedule (PR1)			PM	4				
1.2.4 Gantt chart (PR2)			PM	4				
1.2.6 Updated scope statement (PR2)			PM	2				
1.2.5 Additional sponsor feedback (PR2)			PM	2				
1.3 Executing	Week 3	Week 15						
1.3.1 Communications								
1.3.1.1 Document team meetings			PM	30				
1.3.1.2 Document sponsor meetings/feedback			PM	10				
1.3.1.3 Update Google site			PM	5				
1.3.2 Design database	Week 3	Week 4						
1.3.2.1 Health tracker table			PM / MD	0.5	2			
1.3.2.2 Reminder system table			PM / MD	0.5	2			
1.3.2.3 Medical contacts system table			PM / MD	0.5	2			
1.3.2.4 Emergency information system table			PM / MD	0.5	2			
1.3.3 Design input forms / outputs	Week 3	Week 4						
1.3.3.1 Health tracker system input / output			PM / MD	0.5	2			
1.3.3.2 Reminder system input / output			PM / MD	0.5	2			
1.3.3.3 Medical contacts system input / output			PM / MD	0.5	2			
1.3.3.4 Emergency information system input / output			PM / MD	0.5	2			
1.3.4 Design UI / UX	Week 3	Week 8				45		
1.3.5 Systems implementation	Week 4	Week 10						
1.3.5.1 Health tracker system implementation			MD			16		
1.3.5.2 Reminder system implementation			MD			8		
1.3.5.3 Medical contacts system implementation			MD			6		
1.3.5.4 Emergency information system implementation			MD			6		
1.3.6 Backend / frontend connection	Week 10	Week 11	MD			16		
1.3.7 QA testing	Week 11	Week 13	QA					25
1.3.8 Privacy / data security validation	Week 13	Week 14	QA					25
1.4 Monitoring and Controlling	Week 1	Week 16						
1.4.1 Progress report 1 (PR1)								
1.4.1.1 Fill out progress report template			PM	4				
1.4.1.2 Assemble all documents for PR1			PM	4				
1.4.1.3 Prepare and practice presentation			PM	2				
1.4.1.5 Post all info online			PM	2				
1.4.2 Progress report 2 (PR2)								
1.4.2.1 Fill out progress report template			PM	4				
1.4.2.2 Prepare est. vs. actual hours summary			PM	2				
1.4.2.3 Assemble all documents for PR2			PM	4				
1.4.2.4 Prepare and practice presentation			PM	2				
1.2.2.5 Post all info online			PM	2				
1.4.3 Other monitoring and controlling								
1.5 Closing	Week 15	Week 16						
1.5.1 Project notebook			PM					
1.5.1.1 Assemble all documents for notebook			PM	4				
1.5.1.2 Receive project completion form from sponsor			PM	1				
1.5.1.3 Prepare final report			PM	10				
1.5.1.4 Prepare and practice final presentation			PM	2				
1.5.1.5 Post all info online			PM	2				
1.5.1.6 Final presentation completed (milestone)			PM	1				

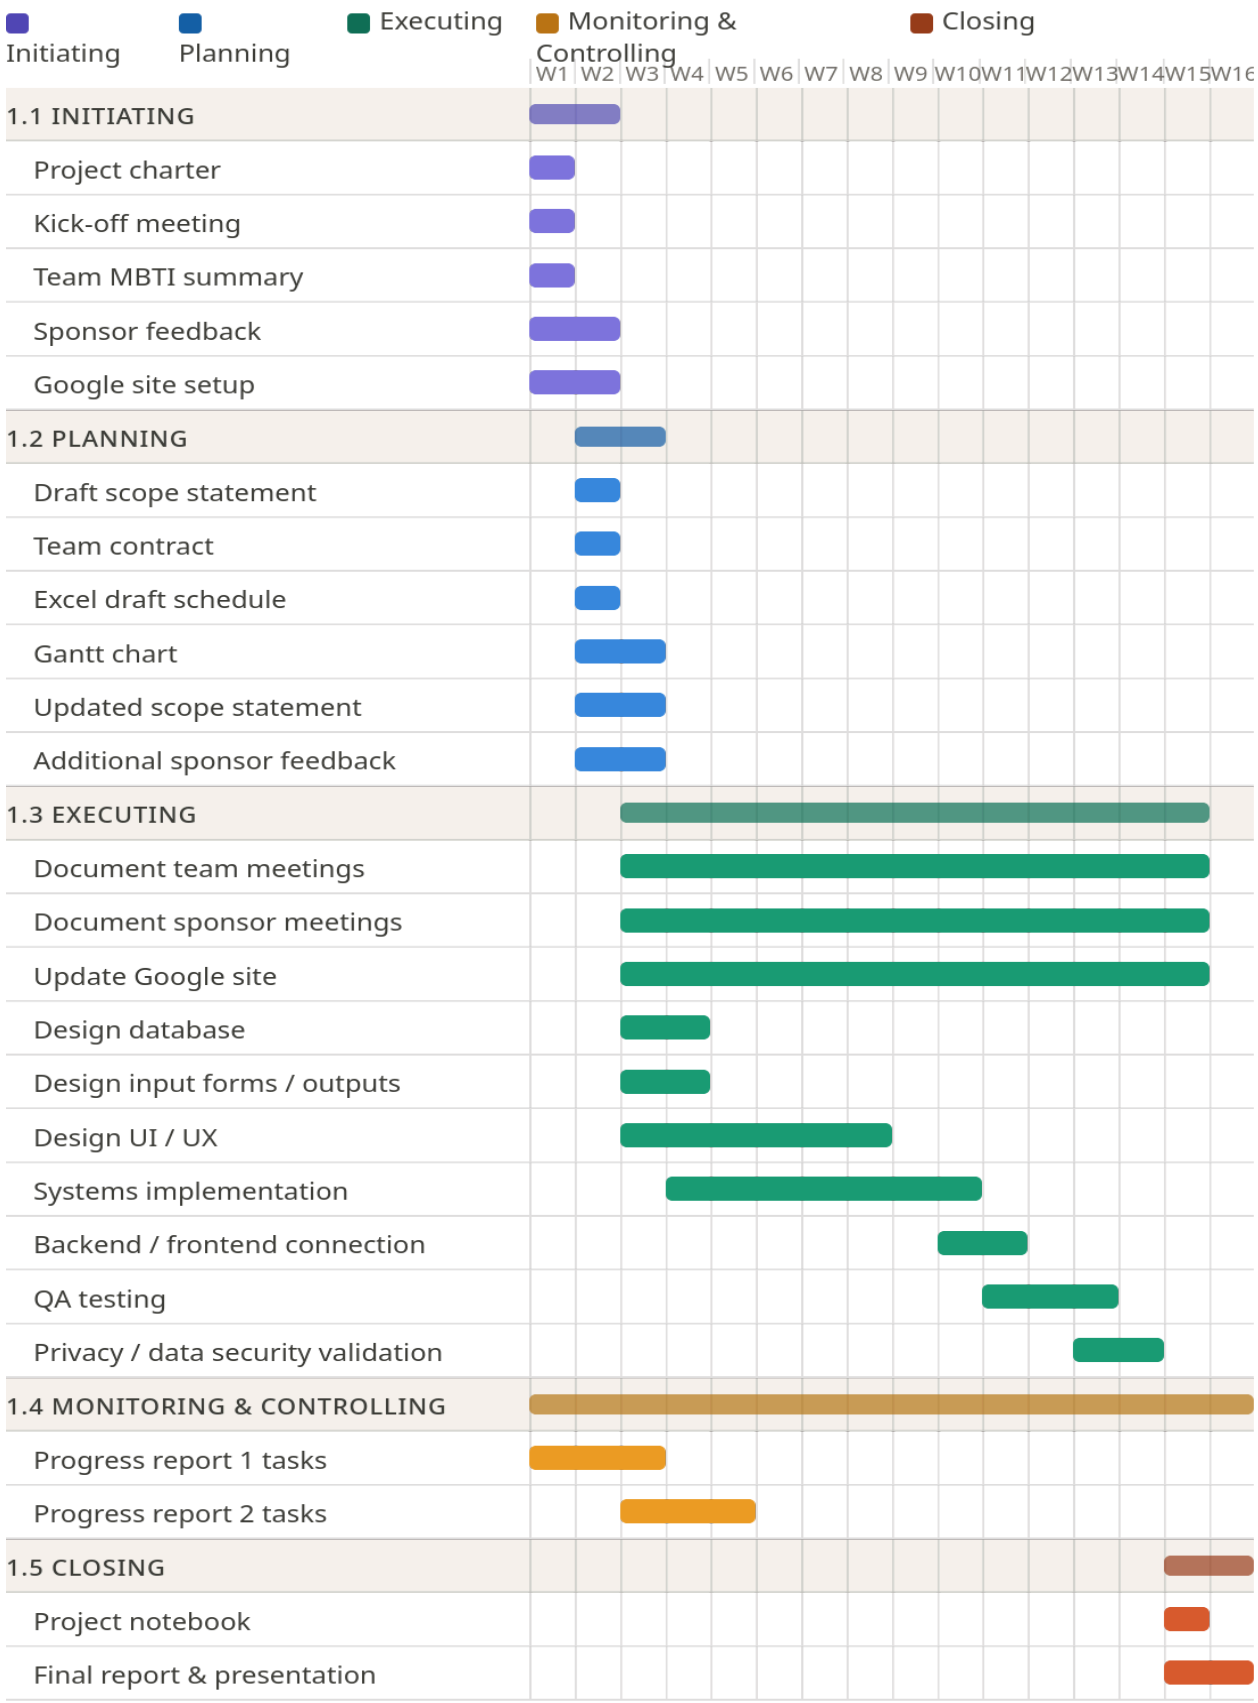
Initiating
Planning
Executing
Monitoring & Controlling
Closing
W1 W2 W3 W4 W5 W6 W7 W8 W9 W10 W11 W12 W13 W14 W15 W16
1.1 INITIATING
Project charter
Kick-off meeting
Team MBTI summary
Sponsor feedback
Google site setup
1.2 PLANNING
Draft scope statement
Team contract
Excel draft schedule
Gantt chart
Updated scope statement
Additional sponsor feedback
1.3 EXECUTING
Document team meetings
Document sponsor meetings
Update Google site
Design database
Design input forms / outputs
Design UI / UX
Systems implementation
Backend / frontend connection
QA testing
Privacy / data security validation
1.4 MONITORING & CONTROLLING
Progress report 1 tasks
Progress report 2 tasks
1.5 CLOSING
Project notebook
Final report & presentation

Chapter 4 - Risk Identification & Analysis

NorthStar Digital - Personal Health Companion App (MVP) | Date: March 28, 2026

4.1 Introduction

Risk management is an important aspect of all projects. The Project Management Institute (PMI) defines risk management as the process for identifying, analysing, and responding to risks that could affect the outcome of a project (PMI, 2021); therefore, increasing the likelihood of successful completion of a project.

The PMBOK Guide identifies two major types of risk associated with a project:

- Individual project risk: risks inherent within the project, such as limited resources and time pressures.
- Overall project risk: the overall impact of uncertainty on a project's environment, including both internal and external influences.

This chapter applies these definitions to the NorthStar Digital Personal Health Companion App project -- a 4-month Agile mobile application development effort for $200,000. Six risks are analysed through qualitative risk assessment and prioritized based upon their potential level of impact, each matched with an appropriate response strategy.

4.2 Risk Analysis Methodology

Qualitative risk analysis is the principal analytical method used in this project. As defined by the PMBOK Guide, qualitative risk analysis is the process of prioritizing individual project risks based upon assessments of both their probability of occurrence and their potential impact upon project objectives (PMI, 2021). Qualitative analysis was chosen over quantitative analysis for several reasons:

- The project was in the early planning phase when analysis began; therefore, no numerical data were available regarding historical failure rates.
- The small team size meant limited funds were available to support formal Monte Carlo simulation or advanced quantitative modelling tools.
- As identified by Kendrick (2015), qualitative assessment is widespread in technology projects at the MVP-stage where speed and clarity are given priority over statistical precision.

All risks are rated on a 1-5 scale for both Probability and Impact. Each risk's score is the product of these two values, classified as follows:

Risk Score	Risk Level	Description
15-25	Critical	Immediate escalation and mitigation required
10-14	High	Senior attention required; active response plan needed
5-9	Moderate	Monitor and manage within normal project processes
1-4	Low	Accept or monitor; minimal action required

4.3 Risk Identification & Analysis

R-01 - Data Security Breach

Rank	#1 of 6
Category	External / Technical
Description	The application stores and retrieves the users' sensitive health information including but not limited to their medical condition(s), allergy(ies) and/or intolerance(s), blood group, emergency contact(s), etc. As such it represents a significant risk with respect to potential malicious hacking attempts to obtain unauthorized access, intercepting data during transmission, or breaching stored information on mobile devices and backend server systems without proper security protocols.
Root Cause	Storage and collection of users' sensitive health information on mobile devices and backend servers without implementing appropriate security protocols.
Triggers	Third-party security audits identifying suspicious activity from login access to attempted unauthorized access to users' sensitive health information.
Probability	Medium (3/5)
Impact	Very High (5/5)
Risk Score	15 - CRITICAL
Response Strategy	Encrypt all users' sensitive health information using end-to-end encryption. Perform frequent penetration testing. Establish role-based access controls. Prior to launching the MVP, develop, implement, and test a comprehensive Incident Response Plan.
Risk Owner	Mobile Developer / QA Lead
Analytical Rationale	Although ranked Medium in terms of likelihood, this threat is ranked Very High in terms of impact because if compromised it could lead to exposure of protected personal health information, financial penalties for non-compliance, loss of public confidence, and permanent reputational damage.

R-02 - Regulatory Non-Compliance (PIPEDA / HIPAA)

Rank	#2 of 6
Category	External / Legal
Description	The App collects personally identifiable Health Information (PHI), and therefore there are potential risks associated with failing to meet Canadian Privacy Law Requirements (PIPEDA) and/or relevant U.S. Regulations (HIPAA) that may apply depending on how the application will be promoted across international borders. Potential sanctions include fines, legal actions, and forced cessation of the App.
Root Cause	No legal review of Data Handling Practices included in the Design Phase; limited knowledge of Health Data Privacy Obligations among Development Team members.
Triggers	Regulatory Body Inquiry; Legal Counsel notification of un-reviewed Data Handling Practices; App Store Compliance Review failure.
Probability	Medium-High (4/5)
Impact	High (4/5)
Risk Score	16 - HIGH
Response Strategy	Hire a lawyer/privacy consultant at the beginning of the Requirements Phase; complete a Privacy Impact Assessment (PIA) prior to launching the App. Include Consent Management and Data Deletion Options as part of the MVP Scope.
Risk Owner	Project Manager
Analytical Rationale	Rated Medium-High Probability since the company is a small startup without an employed Compliance Officer. Rated High Impact since violations of these laws can result in regulatory penalties, injunctions, and reputational harm.

R-03 - Personnel Skill Gap / Understaffing

Rank	#3 of 6
Category	Internal / Resource
Description	The project budget has allocated $90,000 to mobile platform development and $25,000 per role to support both UI/UX Design and Quality Assurance. It is difficult to attract skilled programmers capable of developing software for both Android and iOS within a constrained budget. In addition, several roles have yet to be filled by a qualified candidate.
Root Cause	Budgetary limitations hinder the ability to acquire talented individuals. A cross-functionally structured small team limits the amount of redundancy.
Triggers	A key role is vacant at sprint start; failure to meet velocity goals; programmer reports unfamiliarity with React Native or Swift/Kotlin.
Probability	High (4/5)
Impact	High (4/5)

Risk Score	16 - HIGH
Response Strategy	Hire personnel during the initial two weeks of the project. Cross-train other team members on secondary skills. Utilize Agile sprint review sessions to identify underperformance as soon as possible. Identify contingency contractors to utilize up to the full extent of the $15,000 reserve budget.
Risk Owner	Project Manager
Analytical Rationale	High probability because the project charter identifies unfilled positions and a constrained budget. High impact due to how much influence a single skill gap has on a small team -- an underperforming developer could put an entire sprint back.

R-04 - Compressed Timeline / Schedule Overrun

Rank	#4 of 6
Category	Internal / Schedule
Description	A 4-month timeline from April 1 through July 31, 2026 is overly ambitious for a mobile app intended to be on multiple platforms, encompassing accessibility standards, QA, and all app store review phases for both Android and iOS.
Root Cause	A business-driven timeline targeting early market access; underestimation of the time required to comply with dual-platform development requirements.
Triggers	Month 1 sprint velocity below target; submission to an App Store is denied; QA reveals high-risk issues requiring major rework.
Probability	High (4/5)
Impact	Medium (3/5)
Risk Score	12 - HIGH
Response Strategy	Employ timeboxed Agile sprints with clearly identified goals. When time becomes an issue, de-prioritize non-core functionality as early as possible. Submit to App Stores at least two weeks prior to the final deadline. Proactively use the Contingency Reserve.
Risk Owner	Project Manager
Analytical Rationale	High probability due to the short four-month window relative to scope. Medium impact (not High) as the MVP approach already contains elements of mitigation; an extended timeline may be problematic but will not likely result in a damaged product.

R-05 - Low-Quality MVP / Excessive Defects

Rank	#5 of 6
Category	Internal / Quality
Description	Under schedule pressure, the development team may release an MVP with critical bugs and missing features that will negatively affect early user

	perception and skew the feedback collected, making it difficult to make good decisions for Version 2.
Root Cause	Compressed timeline reduces time allocated to QA activities; insufficient time to test on multiple Android and iOS device variants; feature creep pushed back testing phases.
Triggers	QA log indicates critical defect rate exceeds the established threshold; UAT identifies major usability issues; users report application crashes during demo.
Probability	Medium (3/5)
Impact	Medium (3/5)
Risk Score	9 - MODERATE
Response Strategy	Establish a minimum defect threshold for MVP release within the Definition of Done. Establish dedicated QA sprints. Implement automated testing tools (e.g., Appium) for regression testing across platforms. Ensure the QA lead has early involvement in sprint reviews.
Risk Owner	QA Lead
Analytical Rationale	Medium probability because Agile methodology includes natural quality checkpoints, but the compressed timeline creates real pressure. Medium impact: an early poor release can be corrected in subsequent versions, but it costs time and trust.

R-06 - Limited Market Validation from Target Users

Rank	#6 of 6
Category	External / Market
Description	The primary target audience consists of seniors with little to no smartphone proficiency. Those providing MVP feedback as early adopters will most likely be younger and technically proficient users, and therefore their feedback may not accurately represent the wants or actions of the intended audience.
Root Cause	A digital divide exists between early adopter groups and the desired senior population; lack of formalized user research conducted using older adult test subjects during product design.
Triggers	Age distribution of beta testers is younger than target demographic; all usability testing participants have prior app experience; accessibility issues surface upon launch.
Probability	Medium-High (4/5)
Impact	Medium (3/5)
Risk Score	12 - HIGH
Response Strategy	Partner with community-based organizations or local retirement communities to include older adult users in usability testing. Identify specific accessibility requirements (e.g., WCAG 2.1 AA). Have the Marketing Representative assist in recruiting a representative sample of beta testers from the target demographics.

Risk Owner	Marketing Representative / UI/UX Designer
Analytical Rationale	Probability is Medium-High because recruiting older adult users for beta testing requires extra planning. Impact is Medium as this risk primarily affects future decision-making (Version 2 priorities) rather than first MVP delivery.

4.4 Risk Priority Summary

Rank	ID	Risk Name	Category	Prob.	Impact	Score	Response
1	R-01	Data Security Breach	Technical	Medium	Very High	15 - CRITICAL	Mitigate
2	R-02	Regulatory Non-Compliance	Legal	Med-High	High	16 - HIGH	Mitigate
3	R-03	Personnel Skill Gap	Resource	High	High	16 - HIGH	Mitigate/Accept
4	R-04	Compressed Timeline	Schedule	High	Medium	12 - HIGH	Mitigate
5	R-05	Low-Quality MVP	Quality	Medium	Medium	9 - MODERATE	Mitigate
6	R-06	Limited Market Validation	Market	Med-High	Medium	12 - HIGH	Mitigate

4.5 Conclusion

The six identified risks represent both the internal limitations of the NorthStar Digital project (compressed timeline, limited budget, and limited personnel) as well as the external environmental factors in which a health data application operates. Regulatory compliance and data security ranked first among the risks due to the potential long-term consequences of failure. These two risks potentially present additional legal exposure, financial liability, or loss of reputation to the company that far exceeds the short-term risks associated with this project (Office of the Privacy Commissioner of Canada, 2019).

The risks most likely to negatively affect the project internally include personnel and scheduling. Since there are no buffers within an Agile team, each member's level of performance will have a direct influence on whether or not objectives can be completed during each sprint. Although it has less of an immediate negative effect, the market validation risk does have significant implications for planning future products in terms of road mapping past the MVP.

Each risk was reviewed against its likelihood and severity to assign appropriate mitigation strategies consistent with those of PMI. It is recommended that the risk register remain current through continuous monitoring via sprint retrospectives and formal review at every phase gate.

Chapter 5 - Stakeholder Analysis

5.1 Introduction

One of the biggest reasons projects go sideways is not technical failure -- it is people being surprised. Someone important did not know about a change, a key user was never consulted, or the team built something nobody actually wanted. That is what stakeholder management is designed to prevent.

This chapter maps out everyone who has a stake in the NorthStar Digital Personal Health Companion App -- from the leadership team signing off on the budget, to the older adults who will actually use it on their phones. For each stakeholder, we have looked at what they care about, how much influence they have over the project, and how we plan to keep them engaged throughout the four-month Agile sprint cycle.

5.2 Stakeholder Register

The table below covers ten stakeholders across the project. Some are on the team building the app, some are the people who will use it, and others sit outside the project but have real power over whether it succeeds -- like the app stores and privacy regulators. Each entry explains what that stakeholder cares about, how much influence they have, and what the team plans to do to stay on the right side of them.

Stakeholder Name	Role	Interest in the Project	Influence on Project	Engagement Strategy
NorthStar Digital Leadership Team	Project Sponsor / Executive Stakeholder	Seeing the app launch on time and within the $200,000 budget. Want NorthStar to establish a real foothold in the digital health space and gather positive early-adopter feedback.	High -- they hold the purse strings and have final say on major decisions. If priorities shift or costs spike, they can change scope or pause the project.	Bi-weekly executive status reports covering progress, key risks, and upcoming decisions. Bring them in for milestone approvals.
Project Manager (Oji Nkechi)	Project Manager / Team Lead	Getting the team across the finish line without blowing the budget or the deadline. Keeping sprints on track and catching problems before they become crises.	High -- makes day-to-day calls, assigns work, and keeps the Agile process running. When decisions need to be made quickly, the PM makes them.	Sits at the centre of all communication -- running stand-ups, flagging risks early, and ensuring the sponsor is never caught off guard.

Mobile Developer	Core Development Team Member	Having clear, stable requirements to build from. Wants to know exactly what each sprint needs to deliver and does not want requirements changing mid-feature.	Medium-High -- the quality and speed of what gets built depends entirely on this person. Technical decisions made early will shape the rest of the project.	Involve in sprint planning from day one. Ensure acceptance criteria are clear before development starts. Address blockers quickly to maintain momentum.
UI/UX Designer	Design Team Member	Creating something real people -- especially older adults -- will actually want to use. Cares about intuitive navigation, readable text, and a warm, non-clinical experience.	Medium -- how the app looks and feels directly affects whether users stick with it. Good design can make a simple app feel polished.	Run informal usability check-ins early. Share user personas so design decisions are grounded in real needs. Review wireframes before development starts.
Quality Assurance (QA) Lead	Testing Team Member	Enough time and information to test properly. Wants stable builds, clear 'done' criteria, and the ability to flag issues without being pressured to let things slide.	Medium -- the last line of defence before the app reaches users. A QA lead who finds problems early saves the team from embarrassing post-launch bugs.	Bring QA into sprint reviews, not just at the end. Write test plans early and carve out dedicated testing time -- especially for cross-platform testing.
Marketing Representative	Marketing & Market Research	Understanding what the target audience actually wants so the app lands well. Thinking about launch campaign, early-adopter messaging, and feature-market fit.	Medium -- market insight can shape which features get prioritized. Also drives awareness; a strong launch depends heavily on their work.	Loop them into requirements conversations early. Collaborate on the MVP feedback collection plan well before launch day.
End Users (General Public / Older Adults)	Primary App Users	An app that is easy to understand, does not require a tech background, and keeps personal health information private. Older adults need large text, simple navigation, and	High (indirect) -- without users, there is no product. Their post-MVP feedback will directly shape the next version.	Run a beta testing group before full launch to catch usability issues early. Build a simple in-app feedback mechanism.

		reassurance that their data is safe.		
Healthcare Professionals (Doctors, Pharmacists)	Secondary / Indirect Users	Not being put in an awkward position by the app. They want to trust it is accurate and clear that it is a personal tool, not a medical device.	Low-Medium -- their endorsement carries real weight with users. A doctor saying 'this looks useful' matters a great deal.	Consider a brief consultation during the design phase. Ensure the app includes clear disclaimers that it is not a substitute for medical advice.
App Store Platforms (Apple / Google)	Distribution Channel Partner	The app following their rules -- full stop. Both have strict requirements around privacy, security, and content, and a health app will face extra scrutiny.	High -- if the app does not meet their standards, it will not be published. This is a non-negotiable gate.	Study App Store and Google Play guidelines early in development. Build the submission timeline into the project schedule to avoid a last-minute scramble.
Regulatory Bodies (Privacy Authorities)	Compliance & Governance	Personal health data being handled responsibly and in line with Canadian privacy law (PIPEDA). They set the rules the app has to follow.	High (external) -- failing to comply could mean fines, forced changes after launch, or the app being pulled entirely.	Conduct a privacy impact assessment early in the project. Keep data collection to the minimum needed, encrypt sensitive information, and document compliance decisions.

5.3 Stakeholder Power / Interest Matrix

Not every stakeholder needs the same level of attention. This matrix helps the project manager focus energy where it matters most. Stakeholders with high influence and high interest -- like the end users and the Project Manager -- need to be managed closely. Those with high influence but lower day-to-day interest, like the app stores and regulators, need to be kept satisfied through compliance and proactive planning.

	LOW INTEREST	**HIGH INTEREST**
HIGH INFLUENCE	KEEP SATISFIED -- App Store Platforms, Regulatory Bodies, NorthStar Leadership	MANAGE CLOSELY -- Project Manager, End Users
LOW INFLUENCE	MONITOR -- Healthcare Professionals	KEEP INFORMED -- Mobile Developer, UI/UX Designer, QA Lead, Marketing Rep

5.4 Stakeholder Communication Plan

Good communication does not mean bombarding everyone with updates. It means reaching the right people, with the right information, at the right time. The plan below outlines how the team will stay connected with each stakeholder group without creating unnecessary noise.

Stakeholder Group	Communication Method	Frequency	Responsible Party
NorthStar Leadership	Executive status report, email	Bi-weekly	Project Manager
Project Team (Dev, Design, QA, Marketing)	Sprint planning, stand-ups, retrospectives	Daily / Per Sprint	Project Manager
End Users	Beta program, in-app feedback form	Post-MVP Launch	Marketing Representative
App Store Platforms	Submission documentation, compliance review	Pre-launch (Month 4)	Mobile Developer + Project Manager
Regulatory Bodies	Privacy impact assessment, compliance checklist	Monthly review	Project Manager
Healthcare Professionals	Optional consultation meetings	As needed	Project Manager

5.5 Conclusion

Building a good app is hard enough on its own -- building one while keeping ten different groups of stakeholders happy at the same time is the real challenge. This analysis gives the project team a clear picture of who matters, what they care about, and how to stay connected with them throughout the project.

The Project Manager will keep this register up to date as the project moves through its Agile sprints. If new stakeholders emerge or priorities shift, the plan will be updated to reflect that. The goal is simple: no surprises, and no one left out of a conversation they should have been part of.

References

Kendrick, T. (2015). Identifying and managing project risk: Essential tools for failure-proofing your project (3rd ed.). AMACOM.

NorthStar Digital Solutions. (2026). Personal Health Companion App Project Case Study. Course project handout.

Office of the Privacy Commissioner of Canada. (2019). A guide for individuals: Protecting your privacy. Government of Canada. https://www.priv.gc.ca

Project Management Institute. (2019). Practice standard for project risk management. Project Management Institute.

Project Management Institute. (2021). A guide to the project management body of knowledge (PMBOK guide) (7th ed.). Project Management Institute.

U.S. Department of Health & Human Services. (2023). Summary of the HIPAA security rule. HHS.gov. https://www.hhs.gov/hipaa/for-professionals/security/laws-regulations/index.html
